PALLAVI BOREWELL & DRILLERS

Dealers in : 6½" 4½" Borewells Drilling & Inwell Drilling
All Kinds of Motors & Pumps, Sales & Service

No. 66/8, 1st Main Road, Maruthi Layout, M. G. Road,
Nelamangala Bangalore - 562 123.
Moble : 93412 24311, 90089 87530,



Ref : *Date :* 26.2.24

YIELD REPORT

1. Name and Address of the Party : AEE Ward No 15 Dasarahalli Sub Division BBMP.
2. Borewell Location : Maheshwarinagar
3. Total Depth Drilled : 1134 Feet
4. Casing Pipe : 251 Feet
5. Coupling : 13 Coolers
6. Yield Details :
   a) First Spring Touched at : 415 Feet
   b) Second Spring Touched at : 690 Feet
   c) Third Spring Touched at : 960 Feet
7. Total Yield in G.P.H. : 1600 GPH
8. Remarks : DB-15 Needs Guard

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

For PALLAVI BOREWELL & DRILLERS

M.B. Nirajaiah
Proprietor

5th proof :- L

A. N. CHOWDHARY, M.Sc.,
GEOLOGIST

Phone :
Cell : 98454 73398

SRI SHIRDI SAI CONSULTANTS

10, 3rd Floor, 19th Cross, 14th Main, Revenue Layout, Padamanabhanagar
Bangalore - 560 061.

GROUND WATER INVESTIGATION REPORT

To the Asst Executive Engineer -
BBMP
Dasarahalli Engg Division -

S. No. :

Date : 24.2.2014

1. Name of the Customer
2. Location.
   a) Village Ward No:-15 T St cross Muthyalanagaswamy ar b) Block / Ammati chunty Backside Hesaragatta Road - c) District Bangalore
3. Lithology of the Area — Granetic Schistose in nature -
4. Tophographic Features of the Area — The area was a plain area -
5. Hydrogeological condition of the Area — Good -
6. Geophysical survey result. — By Diving rodders
   a) Type of Method.
   b) No of Soundings Conducted.
   c) Recommended Sounding.
   d) Particulars of formations present in the subsurface/possible ground water zones encountered at
      Around 800'?
      970 - 1000'
      1140 - 1170'
      2
      2
   e) Condition of Ground Water. — Good
7. Type of well Recommended. — Bore well (6 1/2") -
8. Depth Recommended. — OB-15 — 1150 - 1200' -
9. Expected Yield. — 1400 - 1600 GPH -
10. Quality of Water. — Good -
11. Approximate depth at which the water is expected to be met. — Around 800'? - Nearly 170-190' of MS casing may be needed - Strictly Advised -
12. Recommended Type and Length of casing to be inserted.
13. Rain water Harvesting adviced or not
14. Remarks.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಬೆಂಗಳೂರು

Site Plan Map

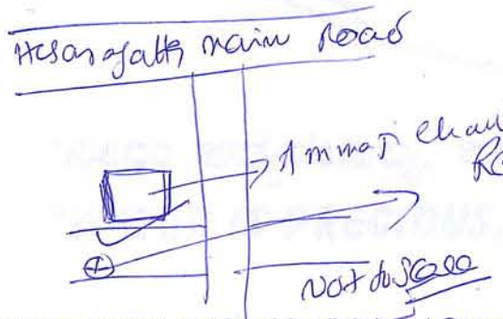

Signature of the consultant

Note :- The Survey was carried out by this divining / Geophysical method of surveying is with our goo knowledge and experience. However no guarantee of water will be given.
